2025 CONSTITUENCY DEVELOPMENT FUND (CDF) COMMUNITY PROJECTS STATUS

MANGANGO CONSTITUENCY

MANGANGO 2025							
S/N	Project Description	Contractor	Ward	Project Amount	Amount Spent	Balance	Physical Status
1	Construction of a 1x3 classrom block at Kaposhi primary school.	Muwema Agencies	Mangango	K1,287,019.00	K609,981.91	K677,037.09	Ringbeam Level
2	Construction of a 1x3 classroom block at Limbotwa-Kasabi primary school.	Kazimire General Dealers	Lukute	K1,389,236.00	0	K1,389,236.00	Mobilization
3	Contruction of a 1x3 classroom block at Mwanambuyu secondary.	Bakwetu	Namafulo	K1,356,507.98	K339,127.00	K1,017,380.98	Ringbeam Level
4	Construction of a 1x3 classroom block at Nyango secondary school.	Built It Africa	Shikombwe	K1,297,344.00	K654,715.38	K642,628.62	Gabble Level
5	Construction of a 1x3 classroom block at Mutondo Primary school.	Litemo Limited	Shikombwe	K1,492,705.52	K373,176.38	K1,119,529.14	Substructure Level
6	Construction of kalundu health post	God's Abundance	Mangango	K1,502,802.00	0	K1,502,802.00	Contract Clearance
7	Construction of nalibako health post	Mude Enterprises	Lukute	K1,439,544.62	K574,675.68	K864,868.94	Window Level With Borehole Drilled And EquiPped.
8	Construction of kalumbelo health post.	Limaroni Business Ventures	Winda	K1,352,404.08	K338,101.02	K1,014,303.06	Substructure Level With Borehole Drilled.
9	Construction of a semi-detched staff house at kafwasonyi.	Lumuli Stationery And Hardware Limited.	Lwambuwa	K674,708.00	0	K674,708.00	Mobilization
10	Construction of a semi-detched staff house at mwanambuyu	Kuka Homes	Namafulo	K625,550.00	K156,387.50	K469,162.50	Mobilization
11	Construction of a semi-detached staff house at mushamba.	Mutulo General Dealers	Nyango	K617,195.88	K154,298.97	K462,896.91	Mobilization
12	Construction of a semi-detched staff house at samukenya primary school.	Zangi Ventures	Lwambuwa	K644,500.00	0	K644,500.00	Mobilization
13	Construction of a local court at lwambuwa.	Lumuli Stationery And Hardware Limited.	Lwambuwa	K548,692.54	0	K548,692.54	Mobilization
14	construction of an ablution block and water reticulation at nyango clinic.	Carnton Builders	Shikombwe	K902,908.60	0	K902,908.60	Mobilization
15	Construction of a semi detached staff house at namishakasha primary school.	Njazu General Dealers Limited.	kapili	K634,950.31	0	K634,950.31	Mobilization
16	Construction of a maternity wing at mushwala Clinic.	MK Kateti Farms	Mushwala	K675,088.00	K168,772.00	K506,316.00	Sub-struture Level

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT KAPOSHI PRIMARY SCHOOL

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT LIMBOTWA PRIMARY SCHOOL

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT NYANGO SECONDARY SCHOOL

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT MWANAMBUYU SECONDARY SCHOOL

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT MUTONDO SECONDARY SCHOOL

CONSTRUCTION OF A HEALTH POST AT NALIBAKO

KAOMA CENTRAL CONSTITUENCY

kaoma central 2025

S/N	Project Description	Ward	Project Amount	Amount Spent	Balance	Physical Status
1	Construction of a 1x3 classroom block at chamiyenge primary school.	Lunyati	K1,242,315.76	K310,578.94	K931,736.82	Window Level
2	Construction of a 1x3 classroom block at Kalumwange Secondary school.	Kalumwange	K1,417,947.12	K354,486.78	K1,063,460.34	Gabble Level
3	Construction of a market shelter at lunyati centre.	Lunyati	K669,852.33	K297,741.00	K372,111.33	Roof Level
4	Construction of a maternity wing at katoya health post.	Chitwa	K633,358.95	K265,812.95	K367,546.00	Roof Level
5	Construction of a 1x3 classroom block at chilombo secondary.	Chilombo	K1,266,456.11	0	K1,266,456.11	Roof Level
6	Construction of a 1x3 classroom block at Mulamatila secondary school.	Mulamatila	K1,280,769.00	K630,263.00	K650,506.00	Roof Level.
7	Construction of a wall fence/ablution block at kalukungu	Mulamatila	K1,233,077.04	K308,269.26	K924,807.78	Ringbeam Level.
8	Construction of an ablution block at luena barracks secondary school.	Mulamatila	K646,319.44	K461,743.48	K184,575.96	Completed
9	Construction of a 1x3 classroom and water reticulation at kashamu secondary school.	Kashamu	K1,683,281.30	K888,920.73	K794,360.57	Roof Level With Water Reticulation Done.
10	Construction of an office block for buildings department.	Mulamatila	K685,502.90	0	K685,502.90	Mobilization (Land Allocation)
11	Construction of a 1x3 classroom block at namaloba secondary school.	Namaloba	K1,317,689.22	0	K1,317,689.22	Substructure Block Work
12	Construction of a 1x3 classroom block at katempe primary school.	Namaloba	K989,713.20	K526,890.15	K462,823.05	Roof Level.
13	Construction of 1x3 classroom block at longe secondary school.	Longe	K1,275,087.96	K318,771.99	K956,315.97	Gabble Level.
14	Construction of a 1x3 classroom block at kalundu primary school.	Mulamatila	K1,230,231.00	K1,087,845.55	K142,385.45	Completed
15	Supply and installation of solar power at Kaoma district hospital.(maternity, female and children's ward)	Mulamatila	K569,659.10	K142,414.78	K427,244.32	Completed
16	completion of naliele palace.	Nalielel	K374,793.54	K337,314.19	K37,479.35	Completed
17	Construction of a 1x3 classroom block at new dawn primary school.	Naliele	K1,047,620.00	K261,905.00	K785,715.00	Roof Level

CONSTRUCTION OF ABLUTION BLOCK AND WALL FENCE AT KALUKUNGU MARKET

CONTRACTOR	CONTRACT PERIOD	CONTRACT SUM (ZMW)	AMOUNT PAID (ZMW)	REMAINING AMOUNT (ZMW)	PROJECT STATUS	CHALLENGES/ RECOMMENDATIONS
Chihinga Ndumba General Dealers.	4 months	1,233,077.04	634,295.95	598,781.09	Installation of palicades remaining for the fence and the ablution block is at window level.	Nil.

CONSTRUCTION OF A 1X3 CLASSROOM AT MULAMATILA SECONDARY

CONSTRUCTION OF AN ABLUTION BLOCK AT LUENA SECONDARY

CONSTRUCTION OF A 1X3 CLASSROOM AT CHILOMBO SECONDARY

CONSTRUCTION OF A MARKET SHELTER AT LUNYATI CENTRE

CONSTRUCTION OF A MATERNITY WING AT KATOYA HEALTH POST

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT KALUMWANGE SECONDARY SCHOOL

PROJECTS UNDER CAPITAL AND ROADS GRANTS STATUS

REHABILITATION OF COUNCIL CHAMBER

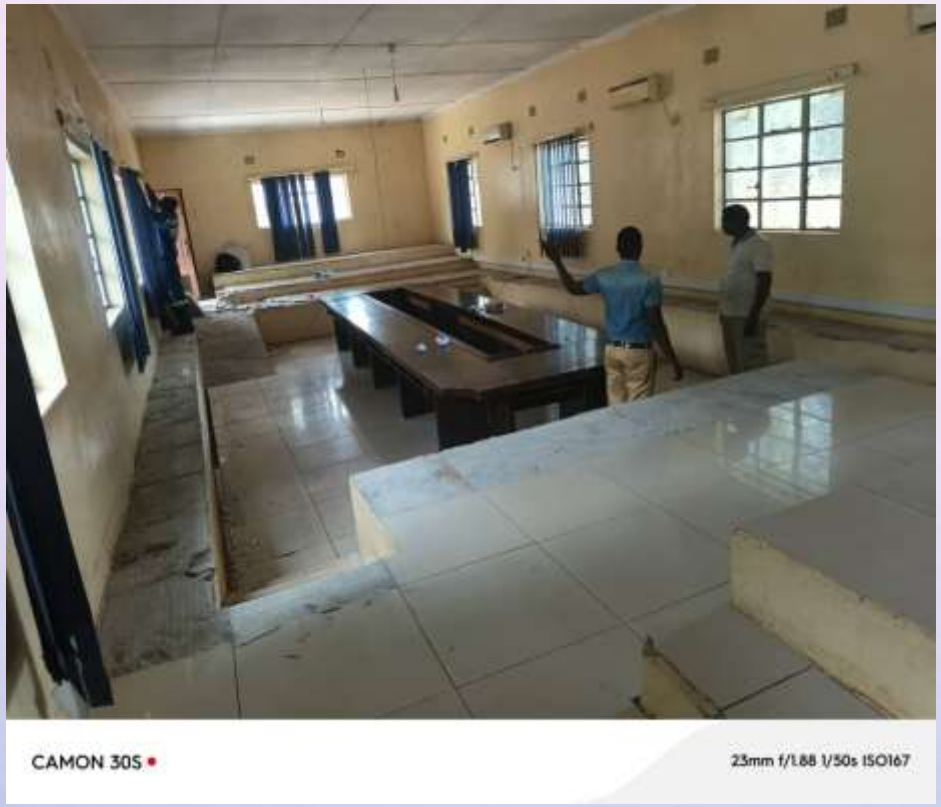

Contractor	Contract Period	Contract Sum (Zmw)	Amount Paid (Zmw)	Remaining Amount (Zmw)	Project Status	Challenges/ Recommendations
Mude Enterprises LTD	4 months	519,917.74	450,439.22	69,478.52	Completed	Nil

THE NEW FACE OF KAOMA TOWN COUNCIL CHAMBER

CONSTRUCTION OF A COMMUNITY HALL

Contractor	Contract Period	Contract Sum (Zmw)	Amount Paid (Zmw)	Remaining Amount (Zmw)	Project Status	Challenges/ Recommendations
Chihinga ndumba general dealers.	4 months	2,315,490.47,	578,872.62	1,736,617.85	Blockwork level	Nil.

WALL FENCE AT COUNCIL DUMPSITE

Contractor	Contract Period	Contract Sum (Zmw)	Amount Paid (Zmw)	Remaining Amount (Zmw)	Project Status	Challenges/ Recommendations
Mude Enterprises Ltd	4 months	6,38370.40	394533.36	43837.04	Complete	Nil

REHABILITATION OF DISTRICT ROADS CDF

On-going road works in Lunyati Road

On-going road works – Mutondo Road

Contractor	Contract Period	Contract Sum (Zmw)	Amount Paid (Zmw)	Remaining Amount (Zmw)	Project Status	Challenges/ Recommendations
Own labour	6 months	6,400,000.00	521,580.00	6,400,000.00	13.4Km Graded	Work stoppages due to inexperienced operators/ New operators have since been employed.

WALL FENCE AT KAOMA TRUCK PARKING BAY

CONTRACTOR	CONTRACT PERIOD	CONTRACT SUM (ZMW)	AMOUNT PAID (ZMW)	REMAINING AMOUNT (ZMW)	PROJECT STATUS	CHALLENGES/ RECOMMENDATIONS
Built It Africa Limited.	4 months	553,660.00	498,294.00	55,366.00	Completed	Nil.

CDF COMPLETED PROJECTS MANGANGO AND KAOMA CENTRAL CONSTITUENCIES

KAKOMBWANA 1X3 CLASSROOM BLOCK

MWANDALEVU 1X3 CLASSROOM BLOCK

MANGANGO MOTHER'S SHELTER

KASHAMU CLINIC STAFF HOUSE

KAMUNI HEALTH POST

NAMIMBWE HEALTH POST

NALIELE PALACE REHABILITATION

CONSTRUCTION OF AN ABLUTION BLOCK AT LUENA SECONDARY

WATER RECTICULATION AT KASHAMU SECONDARY

CONSTRUCTION OF A 1X3 CLASSROOM BLOCK AT KALUNDU PRIMARY
